



GREENBURG

MILESTONE

April 2016

Life Is Peaceful
When amenities are
within your reach



Design & Construction by:



LARSEN & TOUBRO

It's all about Imagination

ULTRA LUXURIOUS CONDOMINIUMS IN SECTOR 86, GURGAON

High-end Specifications



GOLF PUTTING GREENS



2 LARGE SWIMMING POOLS



WI-FI ENABLED TOWERS



20,000 SQ.FT. CLUB HOUSE



8 ACRES - CONTINUOUS RUNNING GREENS



AIR-CONDITIONED APARTMENTS



SS RAILING WITH TOUGHENED GLASS



ITALIAN MARBLE



GROHE/DURAVIT OR EQUIVALENT



COMPLETE SECURITY SYSTEM

#FutureReadyHomes

FIBRE OPTICS IN YOUR APARTMENT



High Speed Connectivity: Up To 100 Mbps Bandwidth Available On Demand To Enjoy Swift Data Download And Video Streaming.

DO YOU FEAR
EARTHQUAKE?



Reinforced Concrete Walls with Mivan Shuttering Technology

HOMES LASTING 100 YEARS

Design & Construction by:



LARSEN & TOUBRO

It's all about Imagineering

Maximum Efficiency



High Carpet Area

#PARADISELIVING



Check Out

Our Newly Designed Website

@

www.microtekinfra.com

GREENBURG

CONSTRUCTION UPDATE

TOWER K



Super Structure completed
Interior plaster work under progress




TOWER L



Super Structure completed
Interior plaster work under progress

TOWER A

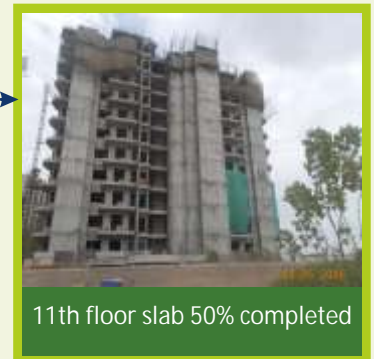

11th floor slab 50% completed

TOWER B



Super Structure completed
Interior plaster work under progress



TOWER D



Super structure completed
Interior plaster work completed

TOWER C



Super Structure completed
Interior plaster work under progress



TOWER I



TOWER J



TOWER E



TOWER H



TOWER G



TOWER F





*TOWER A February 2016
7th floor slab 40% completed*



*TOWER A April 2016
11th floor slab 50% completed*



*TOWER B February 2016
13th floor slab completed*



*TOWER B April 2016
Super Structure completed
Interior plaster work under progress*

Inside your World:

Tile Works - 1st floor completed

Internal Electrical Works - 1st floor completed

Washroom False Ceiling - 1st floor completed



*TOWER C February 2016
Roof floor slab completed*



*TOWER C April 2016
Super Structure completed
Interior plaster work under progress*



*TOWER D February 2016
Super Structure completed
Interior plaster work completed*



*TOWER D April 2016
Super Structure completed
Interior plaster work completed*

*Inside your World:
Tile Works - 1st floor to 4th floor completed
Internal Plumbing Works - 1st floor to 7th floor completed*



*TOWER E February 2016
Super Structure completed
Interior plaster work under progress
Interior finishing work under progress*



*TOWER E April 2016
Super Structure completed
Interior plaster work completed
Interior finishing work under progress*

*Inside your World:
Italian Marble - 1st floor to 3rd floor completed
Tile Works - 1st floor to 19th floor completed
Internal Electrical Works - 1st floor to 5th floor completed
Internal Plumbing Works - 1st floor to 21st floor completed*



*TOWER F February 2016
Super Structure completed
Interior plaster work under progress
Interior finishing work under progress*



*TOWER F April 2016
Super Structure completed
Interior plaster work completed
Interior finishing work under progress
Inside your World:
Italian Marble - 1st floor to 9th floor completed
Tile Works - 1st floor to 21st floor completed
Internal Electrical Works - 1st floor to 17th floor completed
Internal Plumbing Works - 1st floor to 21st floor completed*



*TOWER G February 2016
Super Structure completed
Interior plaster work completed
Interior finishing work under progress*



*TOWER G April 2016
Super Structure completed
Interior plaster work completed
Interior finishing work under progress*

Inside your World:

- Italian Marble - 1st floor to 14th floor completed*
- Tile Works - 1st floor to 21st floor completed*
- Internal Electrical Works - 1st floor to 13th floor completed*
- Internal Plumbing Works - 1st floor to 21st floor completed*
- Washroom Counters - 1st to 2nd floor completed*
- Washroom False Ceiling - 1st floor completed*



*TOWER H February 2016
Super Structure completed
Interior plaster work completed
Interior finishing work under progress*



*TOWER H April 2016
Super Structure completed
Interior plaster work completed
Interior finishing work under progress
Inside your World:
Italian Marble - 1st floor to 18th floor completed
Tile Works - 1st floor to 21st floor completed
Internal Electrical Works - 1st floor to 17th floor completed
Internal Plumbing Works - 1st floor to 21st floor completed
Washroom Counters - 1st floor completed*



*TOWER I February 2016
Super Structure completed
Interior plaster work under progress*



*TOWER I April 2016
Super Structure completed
Interior plaster work completed*

*Inside your World:
Tile Works - 1st floor to 10th floor completed
Internal Plumbing Works - 1st floor to 13th floor completed*



*TOWER J February 2016
Super Structure completed
Interior plaster work under progress
Interior finishing work under progress*



*TOWER J April 2016
Super Structure completed
Interior plaster work completed
Interior finishing work under progress*

*Inside your World:
Italian Marble - 1st floor to 10th floor completed
Tile Works - 1st floor to 13th floor completed
Internal Electrical Works - 1st floor to 13th floor completed
Internal Plumbing Works - 1st floor to 13th floor completed
Washroom False Ceiling - 1st to 7th floor completed*



TOWER K February 2016
Roof floor slab completed
Interior plaster work under progress



TOWER K April 2016
Super Structure completed
Interior plaster work under progress

Inside your World:
Internal Plumbing Works - 1st floor to 3rd floor completed



*TOWER L February 2016
Super Structure completed
Interior plaster work under progress*



*TOWER L April 2016
Super Structure completed
Interior plaster work under progress*

Inside your World:

Tile Works - 1st floor to 3rd floor completed

Internal Electrical Works - 1st floor completed

Internal Plumbing Works - 1st floor to 4th floor completed



GREENBURG SUPER VIEW



